

E-900 Tilt-Up Door Repair

Progress report · San Leandro, CA · Customer identity and exact location redacted

Documented scope

- Document worn E-900 lift hardware, low clearance, and off-track condition
- Remove the old lift hardware and expose compromised jamb framing
- Install pressure-treated 2x6 structural framing
- Reinstall and finish the one-piece door system
- Complete perimeter sealing, hasp work, and final walkthrough

THE VALIANT DOCUMENTATION STANDARD

Before condition, structural repair, and completed installation preserved in one report.

Source: captioned CompanyCam field photos and project footage.

Customer identity, exact address, coordinates, and private notes excluded.

VALIANT GARAGE DOOR

Before Condition

E-900 tilt-up door structural repair progress

Worn E-900 hardware and a hinge pulling away from deteriorated wood.



Before: worn E-900 hinge and spring hardware



Failure: hinge pulling from damaged wood

VALIANT GARAGE DOOR

Access & Disassembly

E-900 tilt-up door structural repair progress

Low clearance and off-track condition documented before hardware removal and framing exposure.



Condition: low clearance and door off track



Disassembly: E-900 hardware removed and framing exposed

VALIANT GARAGE DOOR

Structural Rebuild

E-900 tilt-up door structural repair progress

Pressure-treated 2x6 framing installed and finished before system reinstallation.



Repair: pressure-treated 2x6 framing installed




Repair: finished pressure-treated framing

VALIANT GARAGE DOOR

Completion

E-900 tilt-up door structural repair progress

Perimeter seal, hasp, framing, and completed installation documented at final walkthrough.

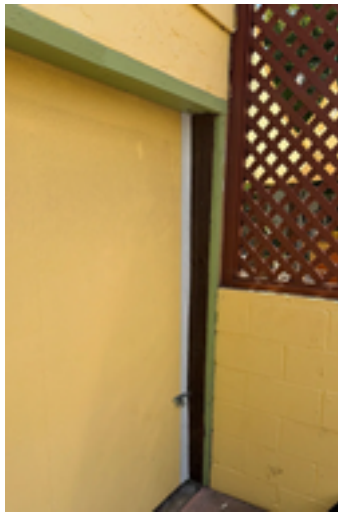

Completion: perimeter seal and hasp finished



Completion: framing and installation finished
